

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/SEMP/01 Last Revision No. 00 Last Revision Date : 00 Page 1 of 8 Original Issue Date :
	Site Specific Environmental Management Plan	

SITE SPECIFIC ENVIRONMENTAL MANAGEMENT PLAN

WBDWSIP BHANGAR-II BLOCK

LOCATION – ZONE-15, PIPE LAYING (Kachua)

0	26.11.2019	<i>for dt. base</i>	<i>dt. base - (Ok. base)</i>	<i>[Signature]</i>	<i>[Signature]</i>
REV	DATE	PREPARED BY	CHECKED BY	APPROVED BY DSISC	APPROVED BY PHJ

Assistant Engineer
PHJ, North 24 Parganas, WBOWSI, PHJ, Dte.
Environmental Specialist, PHJ, Dte.
North 24 Parganas
WBOWSI Project

<p style="text-align: center;">NCC LIMITED</p>	<p style="text-align: center;">Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block</p>	<p>Doc. No. NCC/ SEMP/ 01</p> <p>Last Revision No. 00</p> <p>Last Revision Date : 00</p>
	<p style="text-align: center;">Site Specific Environmental Management Plan</p>	<p>Page 2 of 42</p> <p>Original Issue Date :</p>

[illegible]

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 3 of 42 Original Issue Date :

Details of contractors on-site-personnel and workers	Zone-15 (Pipeline works)/ Chaltaberia GP of Bhangar-II block
Project Manager	Mr. Durga Prasad; 9836803672
Site Engineer	Mr. Amlan Singha Roy; 9734667934
Site Supervisor	Mr. Sain Alam; 9327815543
EHS Supervisor	Mr. Nitin Sartape; 8971107720
Archeological supervisor	NA
Skilled / semi-skilled workers	3 Skilled and 0 Semi-skilled
Unskilled workers	12
Women workers	Nil
Workers – local / migrant	Local-Nil / Migrant-15 (from other districts of West Bengal)
Details of facilities	
Construction camps, (no's and locations)	One labor accommodation at rented house in Sanpukuria [Refer Attachment P2]

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 4 of 42 Original Issue Date :

Table 1: Anticipated Impacts and Mitigation Measures – Pre-construction Environmental Mitigation Plan

Field/ Issues (1)	Anticipated Impact (2)	Recommended Mitigation Measures (3)	Actions Taken/ Status (4)	Responsibility of Implementation (5)	Monitoring of Mitigation (6)	Cost and source of Fund (7)
Infrastructure and Services	Electric poles and wires, water lines within proposed project area of Pipe laying.	<ul style="list-style-type: none"> Locations and operators of these utilities to be identified as per detailed design documents to prevent unnecessary disruption of services during construction phase. Prepare spoils (Waste) management plan. 	<ul style="list-style-type: none"> Contingency Plan has been developed by informing to emergency services like WBSEDCL, Telecommunication, local administration and police etc. First, we are digging the trial pit manually, if any obstruction arise the same is removed as per direction of end user The pipe laying work to continue without disturbing the existing water pipelines and electric poles and overhead HT line. Flagman deployed on-site with Red and Green flags to control traffic and activity side by side. <p>Please refer Attachment P7 and P8 of this SEMP for site specific spoil management plan and traffic management plans respectively.</p>	Contractor, PIU	DSISC observation at site and document checking	Project cost
Climate	The nature and intensity of rainfall events in an area, has implications for surface water management.	Seasonal climatic variations should be taken into account during scheduling of construction in the area.	<ul style="list-style-type: none"> Excavation works schedule during dry season have been approved by PMU. If excavation work is to be conducted during rainy season then preventive measures will be taken like dewatering from the trench During laying use of Gumboot is a must. To avoid slip, trip and fall, no one is allowed within the barrication area. 	Contractor, PIU	DSISC observation at site	Project cost
Sources of Materials	Extraction of materials can disrupt natural land contours and vegetation resulting in accelerated erosion,	<ul style="list-style-type: none"> Obtain construction materials only from government approved quarries with prior approval of PIU. On a monthly basis documentation on material obtained from each source (quarry/borrow pit) should be 	No involvement of any new borrow area or quarry is anticipated. Excavated soil will be used for backfilling of trenches.	Contractor, PIU	DSISC document checking	Project cost

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 5 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	

Field/ Issues (1)	Anticipated Impact (2)	Recommended Mitigation Measures (3)	Actions Taken/ Status (4)	Responsibility of Implementation (5)	Monitoring of Mitigation (6)	Cost and source of Fund (7)
	disturbance in natural drainage patterns, ponding and water logging, and water pollution.	submitted. • In case of involvement of new quarries/ borrow areas, prior steps will follow for all clearances and permissions as required under law.				
Consents, permits, clearances, no objection certificates (NOCs), etc.	Failure to obtain necessary consents, permits, NOCs, etc. can result to design revisions and/or stoppage of works.	<ul style="list-style-type: none"> • All necessary consents, permits, clearance, NOCs, etc prior to award of civil works should be obtained. • All necessary approvals for construction to be obtained before start of construction. • Acknowledge in writing and report on compliance consents, permits, clearance, NOCs etc. obtained. 	<ul style="list-style-type: none"> • We have already received pipelaying permission from local authorities, electric connection, water source etc. • NOC taken from Gram Pradhans for carrying out the activity. • DG sets of capacity less than 5 kVA only being used. • Refer Attachment P3 for relevant clearances. 	Contractor and PIU	DSISC observation at site and document checking	Project cost
Asbestos Cement Pipes	Health risk due to exposure to asbestos materials	<ul style="list-style-type: none"> • Obtain details on location of underground Asbestos Cement pipes • Locate the new pipe carefully to avoid encountering AC pipes • Leave the Asbestos Cement pipes undisturbed in the ground. 	<p>Pipelaying work will be continued without disturbing existing pipelines as recommended in the IEE</p> <p>No asbestos pipes encountered till now. Period. In any circumstances the Asbestos Cement pipes will not be disturbed and left in situ</p> <p>Subproject does not include rehabilitation of existing infrastructure like replacement of AC pipes, tube wells, pumping stations and OHSRs</p>	Contractor and PIU	DSISC observation at site and document checking	Project cost

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 6 of 42 Original Issue Date :

Table 2: Anticipated Impacts and Mitigation Measures – Construction Environmental Mitigation Plan

Field/ Issues (1)	Anticipated Impact (2)	Recommended Mitigation Measures (3)	Actions Taken/ Status (4)	Responsibility of Implementation (5)	Monitoring of Mitigation (6)	Cost and Source of Fund (7)
Material procurement	HDPE pipes gets heated during strong sun and at fusion weld joints.	Hand gloves, nose masks and related PPE's should be used by the workmen.	Continuous supervision regarding the use of safety gadgets is being ensured [Refer Attachment P4 for availability of PPEs at Site].	Contractor	PIU through DSISC observation at site and document checking	Project cost
Air Quality	Emissions from construction vehicles, equipment, machinery and DG set used for excavation and pipe laying resulting in dust and increase in concentration of vehicle-related noxious compounds that causes pollution.	<ul style="list-style-type: none"> Following air pollution/dust control measures for construction activities stipulated by the "Direction of West Bengal Department of Environment under the Air Act, 1981 Direction No. EN/3170/T-IV-7/001/2009 dated: 10 December 2009": <ul style="list-style-type: none"> Only vehicles having valid Pollution Under Control Certificates should be engaged in the project. Vehicles transporting (cement, sands etc) should be covered and cleaned prior to release at site, sprinkling of water and stabilization of soil for dust hazards to be carried out on site. Damp down soil, sand/ earth stockpiled at site should be maintained as per site condition. Control unnecessary movement of vehicle, public trespassing into work areas for control of dust generation. 	<ul style="list-style-type: none"> Only vehicles having valid PUC certificate have been engaged in the project. Sprinkling and dust screen arrangement have been made, and will be used when required. Workers has been instructed to always use dust mask while working in the trench. Site has been access controlled to prevent trespassing. Excavated earth piles will be maintained in such a way to minimise dust rising. Air quality monitoring has been conducted at following five places (Near School Swastayangachhi. Zone-04, Near Paschim Majarhat primary school Shanpukuria. Zone-10, Dharmatala Pachuria Zone:-01 Nangla Palpur Zone:-09) in the Bhangar II Package. 	Contractor	PIU through DSISC observation at site	Project cost
Drainage and hydrology	Due to the nature and locality of the projects there is	<ul style="list-style-type: none"> The site surface should be engineered and shaped in such a way that rapid and efficient 	<ul style="list-style-type: none"> We have ensured run-off through the site to a local drain does not contaminate existing drain and pond around the project site. 	Contractor	PIU through DSISC	Project cost

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 7 of 42 Original Issue Date :

Field/ Issues (1)	Anticipated Impact (2)	Recommended Mitigation Measures (3)	Actions Taken/ Status (4)	Responsibility of Implementation (5)	Monitoring of Mitigation (6)	Cost and Source of Fund (7)
	unlikely to be any significant impacts on water resources within the immediate area.	evacuation of runoff is achieved.	<ul style="list-style-type: none"> Dewatering, if any and hydrotest water, will be also discharged to local drains after ensuring no contamination. 		observation at site and document checking	
River/Surface water quality	Mobilization of settled silt materials, run-off from stockpiled materials, and chemical contamination from fuels and lubricants during construction works can contaminate nearby surface water quality.	<ul style="list-style-type: none"> Avoid stockpiling of earth fill; especially in monsoon season, cover it with tarpaulins or plastic sheets. Prioritize and implement reuse of excess spoil and materials in the construction work; if necessary, dispose in designated disposal area. Storage locations should have impervious floors Fuels and lubricants should be stored away from drainage and spillage protection should be provided. 	<ul style="list-style-type: none"> Excavated earth from dug trenches will be stacked along the pipeline and away from drainage locations/ nearby water bodies. Locations for fuels and lubricants store is away from drainage path and spill kits have been obtained. All excavated soils are expected to be utilized on-site only. No excess spoil anticipated. Surface water monitoring has been conducted already following two places (Koach Pukur Zone:-15, and (Majer hat) Zone-10, Shanpukuria) in the Bhangar II project as per Environmental Monitoring Plan recommended in the IEE. 	Contractor	PIU through DSISC observation at site and document checking	Project cost
Biodiversity Fauna and Flora	Due to the nature and locality of the project there is unlikely to be any significant impacts on bio-diversity within the area.	<ul style="list-style-type: none"> For flora protection, tree cutting is strictly prohibited; if necessary, then obtain permission through proper channel. For faunal activity, instruction should be given to everyone to inform site EHS Coordinator who should take appropriate action for their protection and safe rescue. 	<ul style="list-style-type: none"> Few trees are present along the existing alignment; cutting of tree strictly banned without regulatory clearance, if necessary, trimming allowed. So far no faunal movement has been observed in this site. 	Contractor	PIU through DSISC observation at site and document checking	Project cost
Noise Levels	Increase in noise level due to earth-moving and excavation	<ul style="list-style-type: none"> Minimize noise from construction equipment by using vehicle silencers, fitting jackhammers with noise-reducing 	<ul style="list-style-type: none"> Consultation made with local communities in advance of the work to identify and avoid working at sensitive times, such as religious and cultural festivals. 	Contractor	PIU through DSISC observation at site and	Project cost

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 8 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	

Field/ Issues (1)	Anticipated Impact (2)	Recommended Mitigation Measures (3)	Actions Taken/ Status (4)	Responsibility of Implementation (5)	Monitoring of Mitigation (6)	Cost and Source of Fund (7)
	equipment, and the transportation of equipment, materials by labours	mufflers minimising the sound impact to surrounding sensitive receptor; • Horns not to be used unless it is necessary to warn other road users; • Maintain maximum sound levels not exceeding 75 decibels (dbA). When measured at a distance of 1m from the vehicle/s. • Baseline and construction phase Noise Monitoring (Day & Night time) should be conducted.	• Noise quality Monitoring has been conducted at following five places (Majerhat Sanpukuria Zone:-10, Near Swastayan gchhi School Zone :-04, Dharmatala Pachuria School Zone:-01, Nangla Palpur Zone:-09, Near Coch Pukur Primary School Zone:-15) in the Bhangar Project for Environmental Monitoring Report. • DG set (less than 5 kVA) are used for connecting the HDPE lines. This is properly maintained and stopped immediately after completion of work.		document checking	
Landscape and Aesthetics character, and sense of place	Construction wastes as well as excess construction materials may show some impact.	• Prepare a construction waste management plan for site. • Hazardous wastes e.g. waste oil, empty paint cans, etc. should be stored on site and then shifted to a central location from where these will be disposed in accordance with Hazardous Wastes Management Rule, 2016. • As far as possible utilize the debris and excess soil in construction purpose such as for site filling and labelling purpose. • Avoid stockpiling excavated earth at the site for long time, if required, dispose at the site selected, in consultation with local GP preferably from barren, infertile land, which is located away from any sensitive area.	Landscape and Aesthetics character, and sense of place	Contractor	PIU through DSISC observation at site and document checking	Project cost
Occupational Health and	Occupational hazards which	Develop and implement a site specific occupational health and	• Based on NCC's OHS Plan, a site specific OHS plan has been developed.	Contractor	PIU through DSISC	Project cost

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 9 of 42 Original Issue Date :

Field/ Issues (1)	Anticipated Impact (2)	Recommended Mitigation Measures (3)	Actions Taken/ Status (4)	Responsibility of Implementation (5)	Monitoring of Mitigation (6)	Cost and Source of Fund (7)
Safety	can arise during work	safety (OHS) plan which will include measures such as: (a) excluding public from the site; (b) ensuring all workers are provided with and use personal protective equipment like Helmet, Gumboot, Safety Belt, Gloves, Nose mask etc. (c) documentation of work-related accidents. (d) Providing qualified first aider at all times. (e) Providing to all workers reflective jacket, (f) Marking and providing sign boards for most of hazardous areas such as high voltage equipment, (g) Workers allowed exposure to noise level up to 85 dB (A) only.	<ul style="list-style-type: none"> Site OHS plan is attached at Attachment - P4. All workers have been provided with and made to use Personal Protective Equipment like helmet, gumboot, reflective jacket, gloves, nose mask and ear plugs; H&S Training for all site personnel has been arranged and it will be continued; H&S orientation training provided to all new workers to ensure that they are apprised of the basic site rules of work at the site, personal protective protection, and preventing injuries to fellow workers; Documented procedures are followed for all site activities; Work-related accidents will be recorded; Bottled water provided at site. First Aid box provided at working sites; Clean eating areas provided to workers; Moving equipment maintained with audible back-up alarms 		observation at site and document checking	
Socio Economic Employment	Generation of temporary employment and increase in local revenue	<ul style="list-style-type: none"> Employ local labour force as far as possible Comply with labour laws 	<ul style="list-style-type: none"> Local labours are employed, on priority, whenever available. Refer Attachment P3 for documents relating to statutory compliances 	Contractor	PIU through DSISC observation at site and document checking	Project cost
Environmental Management Plan (EMP) Implementation Training	Irreversible impact to the environment, workers, and community	Project Manager and all key workers will be required to undergo training on EMP implementation including spoils/waste management, Standard operating procedures (SOP) for construction works; occupational health and safety	Training session for all employees has been arranged.	Contractor	PIU through DSISC observation at site and document checking	Project cost

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 10 of 42 Original Issue Date :

Field/ Issues (1)	Anticipated Impact (2)	Recommended Mitigation Measures (3)	Actions Taken/ Status (4)	Responsibility of Implementation (5)	Monitoring of Mitigation (6)	Cost and Source of Fund (7)
		(OHS), core labour laws, applicable environmental laws etc.				
Construction Camps	Temporary air, noise, land and water pollution from machine operation and after establishment of habitation	<ul style="list-style-type: none"> • Camp sites shall be away from residential areas (100 m), sensitive areas (schools, hospitals, etc. 250 m), water bodies (500 m) and forests (more than 1 km) • Use unused, vacant lands; no trees shall be cut • Provide a proper fencing/ compound wall • Prepare a site layout plan & display at the site; uniformly label (name boards) all the places in the facility • Entire site/facility area shall be provided with hard levelled surface as appropriate; no loose soil, slush, water logging etc., • Living quarters and construction camps shall be provided with standard materials; no shacks or huts • Adequate lighting and ventilation • Provide drinking water, water for other uses, and sanitation facilities; drinking water should be regularly tested • Provide clear pathways for safe movement • Provide cooking fuel (cooking gas); and a separate safe place 	<ul style="list-style-type: none"> • Before locating project offices, sheds, and construction plants we discussed with DSISC and within or nearest place has been selected, • Till date no trees have been cut and no any destruction of property, irrigation and drinking water supply systems observed, • Employees are trained for storage and handling of materials which can potentially cause soil contamination and water contamination; • Solid waste managed according to the following preferential hierarchy: reuse, and disposal to designated areas; Kitchen wastes collected in a dustbin then it is disposed outside from area to designated disposal location, • Daily generated effluent disposed by arrangements already present in camp/ household. • The details of labour accommodation are presented in Attachment P2. 	Contractor	PIU through DSISC observation at site and document checking	Project cost

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 11 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	

Field/ Issues (1)	Anticipated Impact (2)	Recommended Mitigation Measures (3)	Actions Taken/ Status (4)	Responsibility of Implementation (5)	Monitoring of Mitigation (6)	Cost and Source of Fund (7)
		to cook; fire wood not allowed • Construct septic tanks and soak pit arrangement for wastewater disposal • Solid waste shall be properly managed – provide separate bins, compost biodegradable waste; sell recyclable waste. • According to rule and regulation camp will be vacated and restored to pre-project conditions before acceptance of work.				
Archaeological and Cultural characteristics	Risk of archaeological chance finds	• Strictly follow the protocol for chance finds in any excavation work; • Construction staff members should be made aware of the likelihood of heritage resources being unearthed and of the scientific importance of such discoveries.	• No archaeological chance finds are reported at project sites till date. • If there is any such finding, action will be taken up as per requirement.			

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 12 of 42 Original Issue Date :


Table 3: Construction Phase Environmental Monitoring Plan for entire package

Monitoring Field	Monitoring Location	Monitoring Parameters	Frequency	Locations*	Cost as per budget (in Rs.)
Ambient air quality	5 locations (to be selected during implementation to represent the overall project area)	<ul style="list-style-type: none"> PM₁₀, PM_{2.5} NO₂, SO₂, CO 	Once before start of construction Quarterly (yearly 4- times) during construction (2- year period considered)	Near School Swastayangachhi. Zone-04, Near Paschim Majarhat primary school Shanpukuria. Zone-10, Dharmatala Pachuria Zone:-01 Nangla Palpur Zone:-09	225,000
Ambient noise	5 locations (same as air quality monitoring)	<ul style="list-style-type: none"> Day time and night time noise levels (24 hours) 	Once before start of construction Quarterly (yearly 4- times) during construction (2- year period considered)	(Majerhat Sanpukuria Zone:-10, Near Swastayan Gachhi School Zone :-04, Dharmatala Pachuria School Zone:-01, Nangla Palpur Zone:-09, Near Coch Pukur Primary School Zone:-15	67,500
Surface water quality	2 locations (to be selected during implementation)	<ul style="list-style-type: none"> pH, Oil and grease, Cl, F, NO₃, TC, FC, Hardness, Turbidity BOD, COD, DO, Total Alkalinity 	Once before start of construction Half yearly during construction (2- year construction period considered)	Koach Pukur Zone:-15, and (Majer hat) Zone-10, Shanpukuria	40,000
Chance Finds	Areas protected by ASI or West Bengal State Archaeology Department	<ul style="list-style-type: none"> Chance finds protocol 	Before finalization of detailed design, consult with ASI or West Bengal State Archaeology Department	-	-

Note: * It should be noted that every quarter only 5 locations in the entire package is monitored for air and noise while two locations are monitored for surface water every half-yearly. Locations are changeable with progress of work. Present locations as mentioned in mitigation tables are base line monitoring conducted as per EMP provision. The exact locations of these monitoring are reported in SEMR over google earth image. For all the packages conduct of these monitoring are responsibility of concerned Contractor and cost for such already budgeted in the IEE.

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhargar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 13 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	

Monitoring Locations on Google Earth

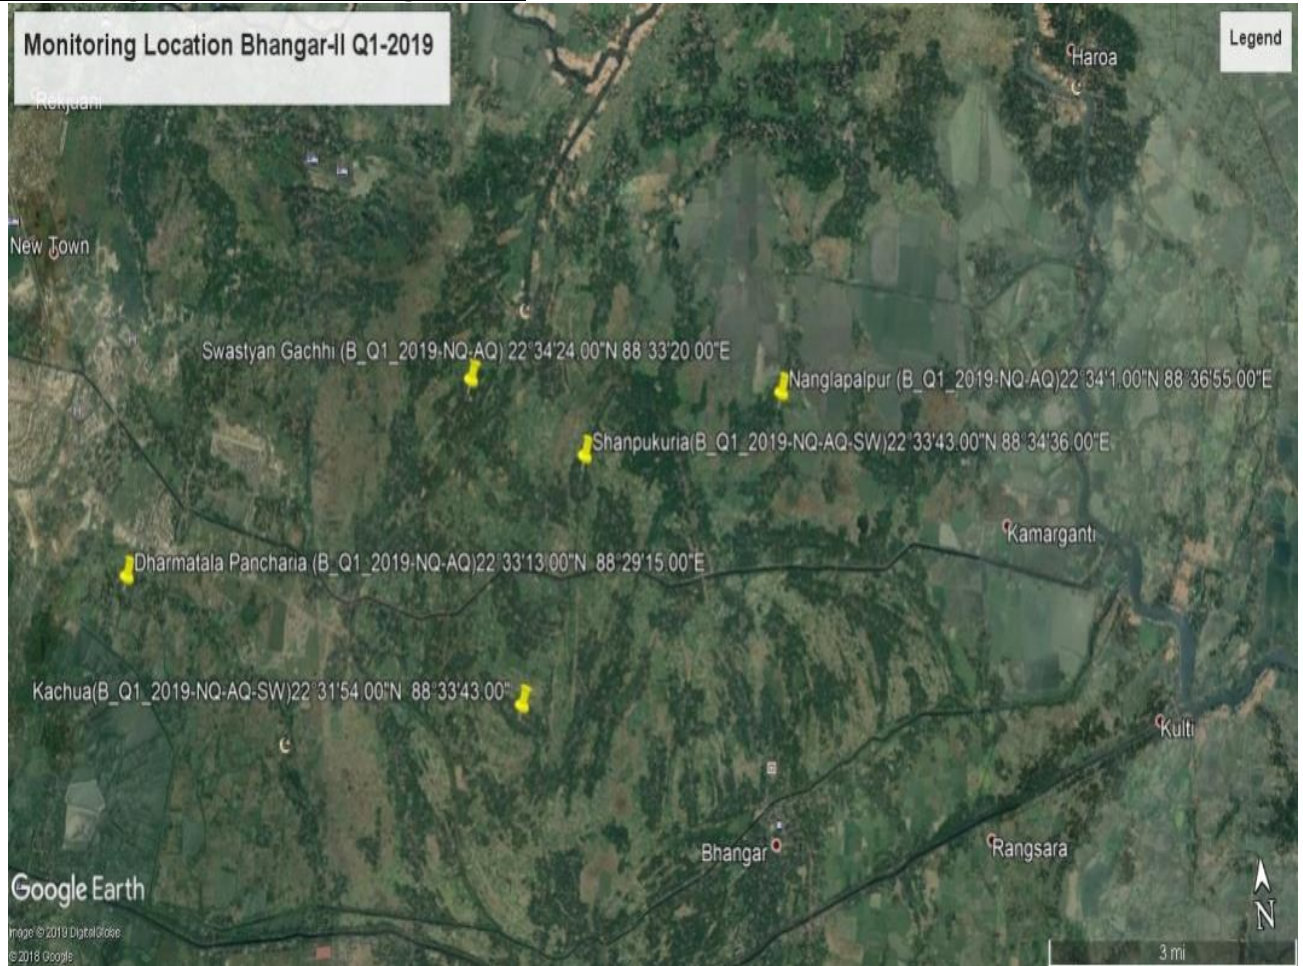

List of Attachments

Attachment P1: Details of construction Work sites
Attachment P2: Details of construction camp sites
Attachment P3: List of clearances & statutory requirements
Attachment P4: Contractor's OHS Policy & Organization
Attachment P5: Utility shifting/relocation
Attachment P6: Details of Construction Materials
Attachment P7: Spoil Management Plan
Attachment P8: Traffic Management Plan
Attachment P9: Procedure for on-site Grievance Redressal Mechanism
Attachment P10: Procedure for information disclosure prior to start of works

Appendix P1: Map of Distribution Network
Appendix P.A: Gram Panchayat and other Authorities Permission
Appendix P.B: Labour License
Appendix P.C: Workman Compensation
Appendix P.D: PUC Certificates
Appendix P.2: Contractor's OHS Policy Statement
Appendix P.3: Sample Grievance Registration Form

Enclosure 1: Health_Safety_Management_Plan of Pkg.N24PGS/02B_Bhargar-II block,



NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 14 of 42 Original Issue Date :

Attachment P1: Details of construction Work sites

1. Zone 15: Pipeline construction Site						
Location- Kachua						
A	Material storage <ul style="list-style-type: none"> • Pipe • Fittings 					
B	Plant & Machinery <ul style="list-style-type: none"> ▪ Jointing Machin-1 Nos ▪ DG (less than 5 kVA) – 1 Nos ▪ JCB-1 Nos 					
C	Site office – No					
D	Laboratory – No					
E	Security cabin – No					
F	Labor welfare facilities at Site <ul style="list-style-type: none"> • Drinking water • First Aid Box. 					
G	Road, agriculture land involvement and infrastructure facility No agricultural land involved No as such underground infrastructure available. No record for village road Details of pipeline, roads and construction methodology are presented below					
	Pipe Diameter (mm)	Length (m)	Width of trench (m)	Depth of Trench (m)	Width of roads (m)	Type of roads (earthen / BT / CC)
	DI Pipes (8209 m)					
	450 mm	313	0.4- 0.8	1.250	2.0-6.0	CC/BT/Earthen
	400 mm	546	0.4- 0.8	1.250	2.0-6.0	CC/BT/Earthen
	350 mm	2744	0.4- 0.8	1.140	2.0-6.0	CC/BT/Earthen
	300 mm	3502	0.4- 0.8	1.30	2.0-6.0	CC/BT/Earthen
	250 mm	1104	0.4- 0.8	1.25	2.0-6.0	CC/BT/Earthen
	Distribution Network— HDPE Pipes(99,982 m)					
	200 mm	8727	0.4- 0.8	1.20	2.0-6.0	CC/BT/Earthen
	140 mm	7160	0.4- 0.8	1.14	2.0-6.0	CC/BT/Earthen
	110 mm	6389	0.4- 0.8	1.11	2.0-6.0	CC/BT/Earthen
	90 mm	9351	0.4- 0.8	1.09	2.0-6.0	CC/BT/Earthen
	75 mm	14430	0.4- 0.8	1.08	2.0-6.0	CC/BT/Earthen
	63 mm	53925	0.4- 0.8	1.06	2.0-6.0	CC/BT/Earthen

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 15 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	

Attachment P2: Details of construction camp sites

1.	Labour Accommodation, Pipeline site – Zone 15	
Location – Labour camp at Sanpukuria in a rented apartment		
A	Accommodation – For 15 construction workers. No women / families in the camp Facilities provided at camp site <ul style="list-style-type: none">• Type of living accommodation – Rented apartment at Sanpukuria• Accommodation provided for 15 workers• Separate cooking area• Cooking gas• Drinking water• Bath rooms• Toilets• Drainage system• First aid box	
B	Camp photographs	
Original site Photographs	Not applicable as rented house is being used as labour accommodation.	
Photos of camp and facilities provided		
	Camp Location rented	Cooking facility at camp

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 16 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	

Attachment P3: List of clearances & statutory requirements

Sl. No.	Project related	Status
A	Construction/work related	
1	Gram Panchayat and Other Authorities Permission	Obtained [Refer Appendix – P.A]
B	Labour Safety / Welfare Related	
1	Labour license	Obtained [Refer Appendix – P.B]
2	Workmen Compensation	Obtained [Refer Appendix – P.C]
C	Safety / liability safety related	
1	Medical insurance	Tie-up with local hospital done
D	Others	
1	Fitness certificate for vehicles, equipment used in construction	Obtained
2	Pollution under control (PUC) certificates for vehicles and equipment	Available [Refer Appendix – P.D]
3	Driving licenses for drivers	Obtained
4	Insurance for vehicles / equipment, as required	Obtained

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 17 of 42 Original Issue Date :

Attachment P4: Contractor's OHS Plan & Organization

1	Contractor agency has a OHS plan	Yes/No	
A	If yes, provide policy details: 1. Policy statement 2. OHS organization & responsibilities:	Yes [Refer Appendix P2] Yes	
B	List safety risks anticipated in the project Area works (Pipeline Work) • Trips and falls • Slope failure / trench collapse • Road accidents Linear works (pipelines) • Accidents from open trenches	-	
C	List personal protection equipment provided to workers • Boots- 18 nos. • Gloves-3 no. • Helmet-16nos. • Safety jacket- 16nos. • Goggles- 2nos.	Yes	
D	Preventive Measures		
	• Orientation of all workers on OSH	Done	
	• Work permit system	No	
	• Toolbox/safety meetings (how often will this be conducted, what are the minimum topics)	Twice Weekly on work inside trench, firefighting, first-aid, housekeeping, etc.	
	• Safety signages	Displayed on site	
	• Barricades (more than 1 m deep requires hard barricading)	Wherever road width permits	
2	Contractor emergency procedure		
A	Detail what steps/procedure to be adopted in emergency situation (eg. accidents) • In case of emergency first aid treatment to injured labour/person shall be provided. • In case hospitalization is required, concerned site in-charge will immediately take necessary action for hospitalization and he will inform to our Project Manager. • Details of accident shall be reported in accident register and the same shall be informed to client also.	Yes	
B	Contact information, staff and responsibilities for emergency situations		
	Designation	Staff name & contact	Emergency responsibility
	Site Engineer	Mr. Amlan Singh Roy Mob: 9734667934	Site Engineer shall be responsible for arranging of first aid treatment and other necessary action required in case of emergency. He will also be responsible for informing to EHS Supervisor.
	EHS Supervisor	Mr. Nitin Kumar Mob: 8971107720	EHS Supervisor should assess the emergency situation and accordingly instruct the Site Engineer of appropriate actions. Depending on the gravity of the situation, he should also inform Project Manager Representative.
	Project Manager Representative	Druga Prasad Mob: 9836803672	Project Manager Representative shall be responsible for taking all necessary action and decisions.
C	Reporting procedure in case of work accidents • Details of accidents shall be recorded in accident register. • Copy of accident register shall be submitted to client at the end of every month. • In case of any major accident client shall be informed immediately.	Yes	
D	Mandatory Reporting to Authorities	Yes	
E	Prohibited Acts and Penalties for Violations	Yes	

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 18 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	

Attachment P5: Utility shifting/relocation

Sl. No.	List work sites that require utility shifting, relocation, temporary shut off	Remarks
1	Area work sites (Pipeline)	Not Required

Attachment P6: Details of Construction Materials

Sl. No	Material	Approximate quantity required (m3) for project	Source	Indicate if source has all necessary government clearances
1	Earth	35418.20	From trench cutting	Not required

(Pipe details are provided in Attachment P1)

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhargar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 19 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	


Attachment P7: Spoil Management Plan

NCC LIMITED	Design and Construction of Reservoir Including Water Supply Distribution Network and Metering Work in Bhargar-II Block	Doc. No. NCC/ SMP /01 Revision No. 00 Revision Date : 00 Effective Date : Page 1 of 5
	Spoil Management Plan	

SPOIL MANAGEMENT PLAN (SMP)

WBDWSIP BHANGAR-II BLOCK

LOCATION – ZONE-15, PIPE LAYING (KACHUA)

0	26.11.2019				
REV	DATE	PREPARED BY	CHECKED BY	APPROVED BY DSISC	APPROVED BY PIU

Environmental Specialist, DSISC
 North 24 Parganas
 WBDWSI Project
 Assistant Engineer - II
 PIU, N-24Pgs. WBDWSIP, PHE DE
 Govt. Of West Bengal

West Bengal Drinking Water Sector Improvement Project

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 20 of 42 Original Issue Date :

1. INTRODUCTION OF SMP:

SMP is to describe how the project will manage the spoil generated and reuse related to design and construction works. This is an integral part of EMP. The objective of SMP is to reuse of spoil from works.

2. SCOPE:

This Spoil Management Plan developed for pipeline network laying in Zone (15). For Pipe line work we do not anticipate any excess Spoil for disposal as all excavated material will be reuse at site only

3. LEGAL AND OTHER REQUIREMENTS:

In this project, there is no legal litigation at site for land and working area or site. Disposal of spoil will confirming the Environmental Protection Rules and Regulations of Govt. Of India and the State Govt.

4. ROLES AND RESPONSIBILITY:

SITE ENGINEER:

- Will strictly work as per drawing.
- Will stay at site during activity is going on.
- Will see excess earth is kept at a particular place after completion of backfilling.
- Will ensure quality of the work by discussing daily about the type of activity on that day with the workmen.
- Will check site drain outlets are not blocked due to excavated earth on the drain.

SAFETY PERSONNEL:

- Will constant Job specific Tool Box Talk with Supervisor and Workmen.
- Will check excavated earth kept away from top.
- Will check if any underground pipeline is there or live electric cable there water should be sprayed to avoid dust hazard from excavation.
- Necessary Safety signage, Cones to be used.
- Vehicles reverse horn etc to be checked will ensure zero tolerance in safety.

WORKER:

- Workers will start activity only after job specific Tool Box Talk done by the job supervisor.
- They will wear job specific safety items before start of work.
- During working inside the excavated trench, they should use ladder for easy access.
- They should barricade the area of activity with Safety barricading tape/Safety cone/ Caution Boards at the start and end of a road under excavation
- Worker should be skilled to carry out the work.
- Workers should take care of the pedestrians and vehicles safe movement.

It is the responsibility of the Engineers and all department head to implement this procedure and ensure that delegated staff and worker under their supervision carry it out in this project. Major roles and responsibilities are mentioned below:

- Excavated earth should be utilized like refilling at site only.
- Traffic movement should not be obstructed by dumping soil during the work.
- No low land, pond, ditch etc. will be filled up by extra soil outside the work place.
- Ensuring no accident occurs during rainy season by excavated earth during or finished the

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 21 of 42 Original Issue Date :

work.

- All the drains, outlet should be free from excavated earth.

5. IDENTIFICATION AND ASSESSMENT OF SPOIL ASPECTS AND IMPACTS:

In this project, there are some places which will be assessed and identified jointly along with design engineer. Main places where the excavated earth can be utilized are the trench of pipes and backfilling location.

6. SPOIL VOLUMES AND CHARACTERISTICS:

In this project, approx. Generation of excavated earth will be approx. 35418.20 cum. There is no excess earth in this project as the same earth is to be used to fill the low land area.

As per report from soil expert, excavated earth is cohesive in nature.

7. SPOIL REUSES OPPORTUNITIES, IDENTIFICATION AND ASSESMENT:

In this project, there is no excess quality of excavated earth; total excavated earth should be reuse as per plan.

8. ON SITE SPOIL MANAGMENT APPROACH:

In this project, no need of the approach as there is any extra soil for disposal.

9. SPOIL TRANSPORTATION METHODOLOGY:

In this project, no need for transport as there is no extra soil for disposal.

10. MONITORING, REPORTING, REVIEW AND IMPROVEMENTS:

Monitoring, Reporting and all necessary improvements will be done as per requirements.

Expected Spoil generated at Kachua (Zone 15) for Pipe laying

Sl. No.	Dia	Length(m)	Width(m)	Depth(m)	Total(cum)
1	63	53925	0.3	1	16177.50
2	75	14430	0.3	1	4329.00
3	90	9351	0.3	1	2805.30
4	110	6389	0.3	1	1916.70
5	140	7160	0.3	1	2148.00
6	200	8727	0.4	1	3490.80
7	250	1104	0.5	1	552
8	300	3502	0.5	1	1751.20
9	350	2744	0.6	1	1646.40
10	400	546	0.7	1	382.20
11	450	313	0.7	1	219.10
Approx. generated total Spoil at Zone-15					35418.20

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00
	Site Specific Environmental Management Plan	Page 22 of 42 Original Issue Date :





Attachment P8: Traffic Management Plan

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ TMP /01 Revision No.00 Revision Date : 00 Page 1 of 7 Effective Date :
Traffic Management Plan		

TRAFFIC MANAGEMENT PLAN (TMP)

WBDWSIP BHANGAR-II BLOCK

LOCATION – ZONE-15,PIPE LAYING (Kachua)

0	25.11.2019				
REV	DATE	PREPARED BY	CHECKED BY	APPROVED BY DSISC	APPROVED BY PIU

Environmental Specialist, DSISC
 North 24 Parganas
 WBDWSI Project

West Bengal Drinking Water Sector Improvement Project

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 23 of 42 Original Issue Date :

1. **PURPOSE**

Main purpose is to prevent accident between vehicles, pedestrians and employees and also minimise inconvenience to the vehicle. To stop property damage and prevent injury to persons arising from site traffic and site transport.

2. **SCOPE**

The procedure is applicable for HDPE/DI pipe laying area. Pipelaying works not required full road closure but partial closure is required on all these roads and hence, traffic management plans have been developed accordingly

3. **RESPONSIBILITY**

It is the responsibility of the Engineers and all department head to implement this procedure and ensure that delegated staff under their supervision carries it out.

4. **LEGAL REQUIREMENT**

The Building and Other Construction Workers (Regulations of Employment and Conditions of Service) Act 1996 and Central Rule 1998 Rule 48, 88 and 95, Motor Vehicle Act 1988

5. **REQUIREMENTS**

5.1 **General**

- All road works create inconvenience and are a potential hazard to the safety of all road users and those employed in carrying out the work.
- All the effects should be reduced to the minimum, and to ensure that the works are properly guarded, lighted and signed.
- A clear and early warning of any obstruction to all road users should be provided.
- All areas where work is going on should be clearly demarcated by proper barricading and entry into these areas should be restricted to only authorize personnel.
- Site access for local people.

5.2 **Planning Stage**

Particular attention should be given to:

- Traffic signs
- Cones
- Barriers
- Road hazard warning lights
- Information boards and
- Site lighting
- Site access for local people
- Consider necessity to traffic control systems such as temporary traffic lights or Stop/Go boards.
- Access should be planned to eliminate dangerous movements of site traffic (e.g. reversing of vehicles) and personnel (e.g. crossing dual carriageways).
- Provision of adequate lighting while working at night.
- All persons working on the road shall wear high visibility jackets.

5.3 **On Site**

The working space shall be defined and "A PLACE FOR EVERYTHING AND EVERYTHING IN ITS

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 24 of 42 Original Issue Date :

PLACE” to be follow.

5.4 Operators/Drivers

- Only Experienced operators and drivers with valid licensed has been appointed.
- One copy of license has been collected.
- Refreshment training conducted for all operators and drivers.
- Operators/Drivers authentication and validation to operate the particular machinery displayed in the machine/vehicles.

5.5 Equipment

- Drivers undertake a daily visual inspection of their vehicles include steering, brakes, mirrors, lights, horn, tyres and windshield wipers.
- Safety Department along with Plant and machinery department shall check the vehicles as a monthly basis.
- All vehicles have reverse horns and it is in working properly.
- All vehicles, preventive maintenance schedule has to be followed strictly.

5.6 Roads

- For safe operation we are following the below safety measure:
- Safe width of road has been provided.
- Flag man deployed at every traffic point to control the vehicles and pedestrians.
- Speed limits 10km/hr within the working area.
- Caution board has been placed in every location within the site.
- Workers are working with reflective jacket as well as required PPE's.
- Road for use of pedestrian has been identified.
- Reverse horn used in vehicles.
- While reverse vehicles ensuring Banks man.
- Do's and Don'ts displayed at site office.


5.7 Loading and Unloading

- Only authorized persons were engage loading/unloading.
- Materials loaded within the permitted safe weight limit (as per RTO) for the truck.
- Ensuring Soil and Sand loaded trucks are covered with tarpaulin while transporting
- During Toolbox talk's intimation has been delivered to all drivers/operators that when the drivers leave the driving seat, the engine of the truck shall be switched off, the gear engaged and parking brakes applied. On slopes, wheel blocks shall be applied.
- Helper has been provided with all vehicles.
- After unloading, the banks man ensuring that the tipper is lowered before moving.
- Turn buckle and side stoppers used while transporting as required.


5.8 Working Area

- The working area has been restricted from unauthorized entry.
- The working space has been defined.
- Particular attention has been taken in working area:
- Traffic signs
- Cones
- Barriers
- Information boards, and
- Site lighting
- Adequate lighting has been provided at working area at night.
- All persons wear high visibility jackets.

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 25 of 42 Original Issue Date :

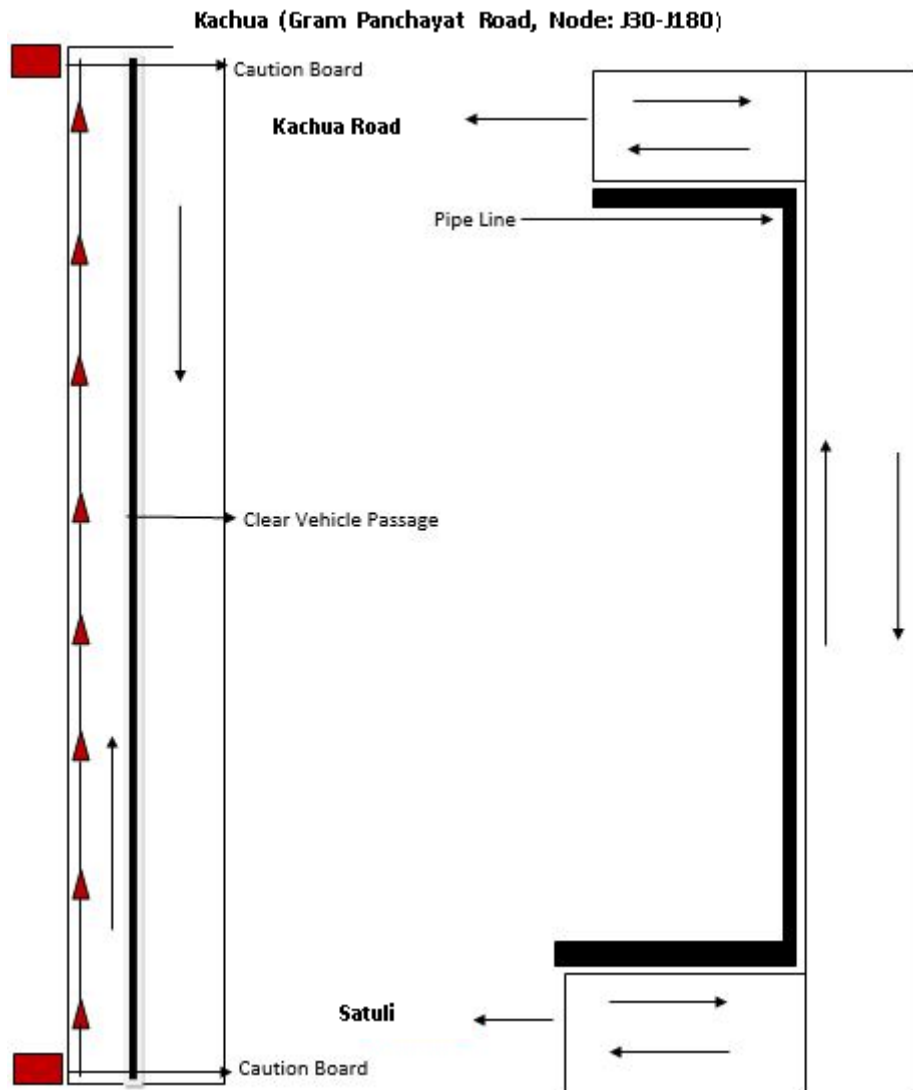

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 26 of 42 Original Issue Date :

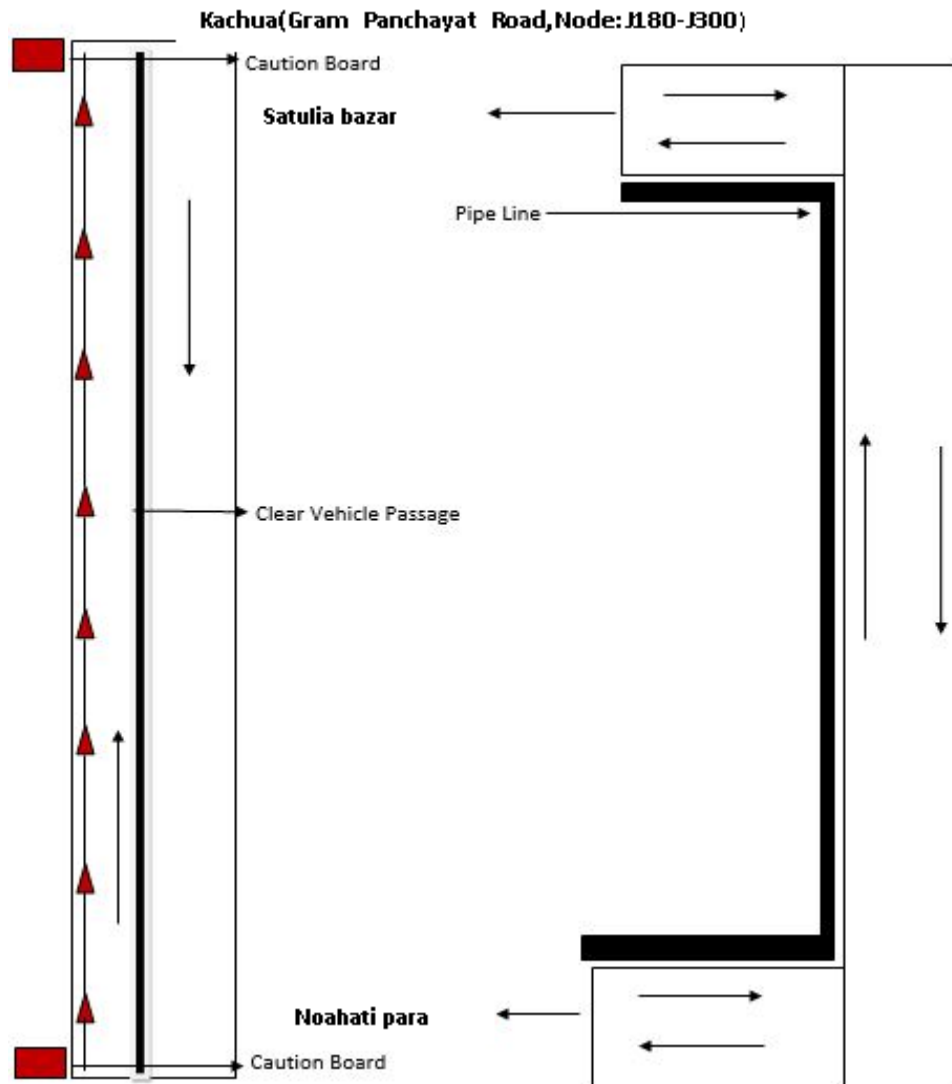


NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhargar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 27 of 42 Original Issue Date :

Attachment P9: Procedure for on-site Grievance Redressal Mechanism

A common Grievance Redressal Mechanism (GRM) is in place to redress social, environmental or any other project and/or subproject related grievances. The GRM presented below has been developed in consultation with stakeholders. Public awareness campaign has been conducted to ensure that awareness on the project and its grievance redress procedures is generated. The campaign has ensured that the poor, vulnerable and others are made aware of grievance redress procedures and entitlements per project entitlement matrix, and PMU and PIU will ensure that their grievances are addressed in time.

Grievance Redress Mechanism

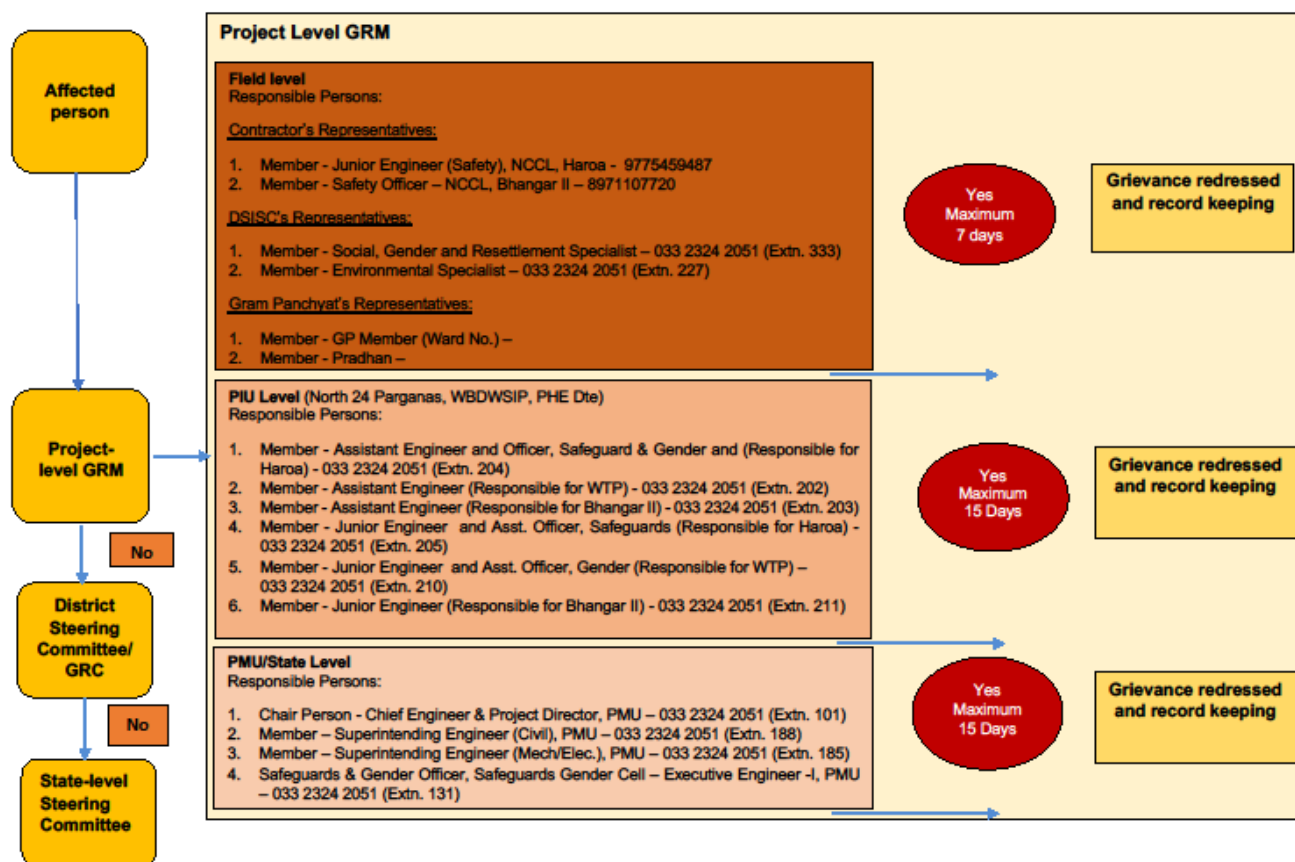


All grievances are recorded in site grievance register and resolved at the earliest. The sample grievance registration form is included in Appendix P3.

Attachment P10: Procedure for information disclosure prior to start of works

- Local population is informed through community leaders as well as by visiting individual households of the locality.
- Information board is placed at construction site
- Stakeholder consultation carried out at Gram Panchayet level and work details including time period is informed.


NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 28 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	

Appendix P.1: Map of Distribution Network

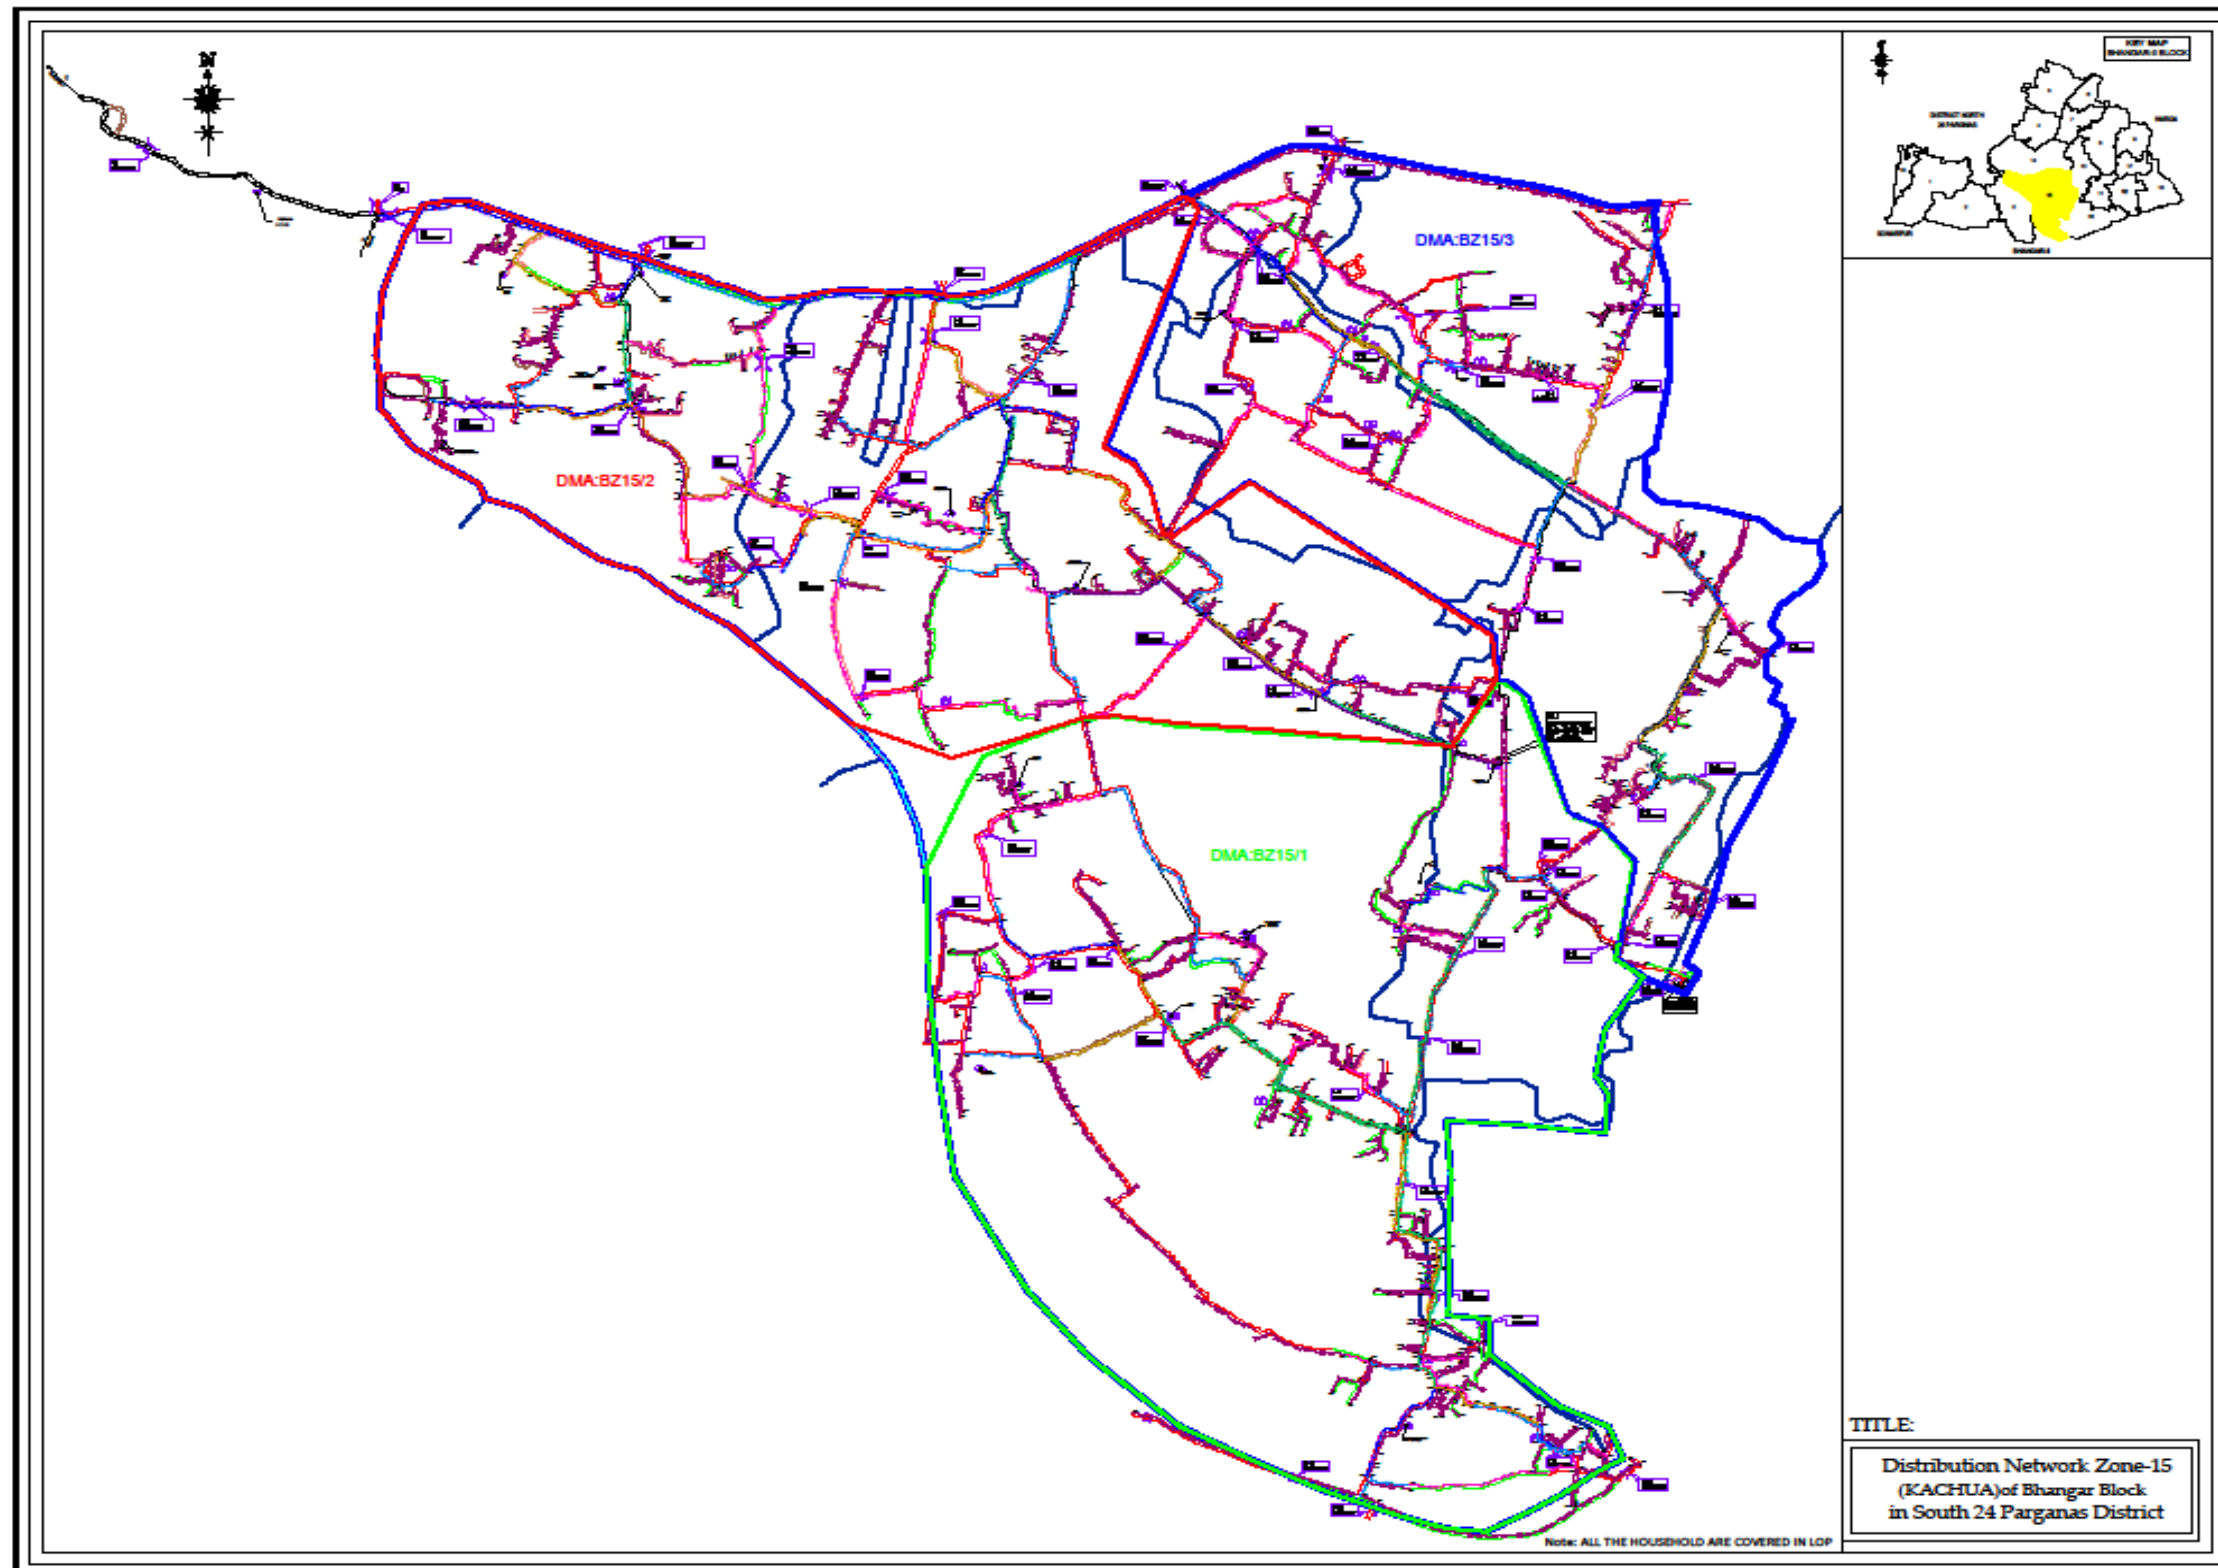

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangan-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 29 of 42 Original Issue Date :

Appendix P.A: Gram Panchayat and other Authorities Permission


Government of West Bengal
Office of the Executive Engineer
PIU, North 24 Parganas, WBDWSIP, PHE Dte.
Utility Building, Tank No.3, 2nd Floor, Block-AI,
Action Area-IA, New Town, Kolkata-700156
Phone No. : (033) 2324-2051, E-mail : ee.piun24p.adb@wbphed.gov.in

Memo No. _____/EE(C)PIUN24P. Dated, New Town, the, _____

To
The District Engineer,
South 24 Parganas Zilla Parishad,
Aijour, South 24 Parganas.

Sub. : Design and construction of overhead reservoir including water supply distribution network & metering works in Bhangan-II Block (Zone-15) **Kachua**.

Dear Sir,

This is to inform you that, PHE Dte. has undertaken a water supply project in the month of October'2018 in Bhangan-II block under the financial assistance of ADB and laying of foundation stone of the same was done by Hon'ble Chief Minister of West Bengal on 26th October'2018. Now the entrusted agency will start the laying of distribution network from 16.12.2019 in **Blugabanpur & Chaltaberia Gram Panchayat** along the road under your jurisdiction within the ROW and a copy of distribution network drawing is herewith enclosed for ready reference.

Your kind co-operation in this regard is requested.

Encls. : As stated.

Yours faithfully,

Sd/-
Executive Engineer,
PIU, N-24 Pgs., WBDWSIP, PHE Dte.
Dated, New Town, the, _____

Memo No. _____/EE(C)PIUN24P,
Copy forwarded for information to :

- 1) The Sabhalupati, South 24 Parganas Zilla Parishad.
- 2) The District Magistrate, South 24 Parganas

Sd/-
Executive Engineer,
PIU, N-24 Pgs., WBDWSIP, PHE Dte.
Dated, New Town, the, 13/12/2019

Memo No. 1139 (2-3)/EE(C)PIUN24P,
Copy forwarded for information to :-

- 1) The Superintending Engineer, P.I.U., North 24 Parganas, WBDWSIP, P.H.E. Dte.
- 2) The Assistant Engineer-II, PIU, N-24 Pgs., WBDWSIP, PHE Dte.
- 3) The Team Leader, DSISC-North 24 Parganas, WBDWSIP.
- 4) The Project Manager, NCC Ltd., Bhangan-II Project.

Sd/-
Executive Engineer,
PIU, N-24 Pgs., WBDWSIP, PHE Dte.

2467
16/12/19

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhargar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 30 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	



**Government of West Bengal
Office of the Executive Engineer
PIU, North 24 Parganas, WBDWSIP, PHE Dte.
Utility Building, Tank No.3, 2nd Floor, Block-AI,
Action Area-IA, New Town, Kolkata-700156
Phone No. : (033) 2324-2051, E-mail : ee.pium24p.adb@wbphed.gov.in**

Memo No. _____/EE(C)PIUN24P,

Dated, New Town, the, _____

To
The Executive Engineer,
WBSRDA,
South 24 Parganas Unit.

Sub. : Design and construction of overhead reservoir including water supply distribution network & metering works in Bhargar-II Block (Zone-15) Kachua.

Dear Sir,

This is to inform you that, PHE Dte. has undertaken a water supply project in the month of October'2018 in Bhargar-II block under the financial assistance of ADB and laying of foundation stone of the same was done by Hon'ble Chief Minister of West Bengal on 26th October'2018. Now the entrusted agency will start the laying of distribution network from 16.12.2019 in **Bhagabampur & Chaltaberia Gram Panchayet** along the road under your jurisdiction within the ROW and a copy of distribution network drawing is herewith enclosed for ready reference.

Your kind co-operation in this regard is requested.

Encls. : As stated.

Yours faithfully,

Sd/-
Executive Engineer,
PIU, N-24 Pgs., WBDWSIP, PHE Dte.

Memo No. _____/EE(C)PIUN24P,

Dated, New Town, the, _____

Copy forwarded for information to :-

- 1) The Sabhachipati, South 24 Parganas Zilla Parishad.
- 2) The District Magistrate, South 24 Parganas.
- 3) The District Engineer, South 24 Parganas Zilla Parishad.

Sd/-
Executive Engineer,
PIU, N-24 Pgs., WBDWSIP, PHE Dte.

Memo No. 11/10/3-2/EE(C)PIUN24P,

Dated, New Town, the, 13/12/2019

Copy forwarded for information to :-

- 1) The Superintending Engineer, P.I.U., North 24 Parganas, WBDWSIP, P.H.E. Dte.
- 2) The Assistant Engineer-II, PIU, N-24 Pgs., WBDWSIP, PHE Dte.
- 3) The Team Leader, DSISC-North 24 Parganas, WBDWSIP.
- 4) The Project Manager, NCC Ltd., Bhargar-II Project.

Sd/-
Executive Engineer,
PIU, N-24 Pgs., WBDWSIP, PHE Dte.

RECEIVED
Time - 10:41 AM
Date 16/12/19

2468
Sd/-
Signature

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhargar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 31 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	



**Government of West Bengal
Office of the Executive Engineer
PIU, North 24 Parganas, WBDWSIP, PHE Dte.
Utility Building, Tank No.3, 2nd Floor, Block-A1,
Action Area-1A, New Town, Kolkata-700156**

Phone No. : (033) 2324-2051, E-mail : ee.pjun24p.adb@wbphed.gov.in

Memo No. _____/EE(C)PIUN24P,

Dated, New Town, the, _____

To
The Divisional Manager,
Bhargar Division, WBSEDCI,
Ghatatpukur, South 24 Parganas.

**Sub. : Design and construction of overhead reservoir including water supply distribution
network & metering works in Bhargar-II Block (Zone-1S) Kachua.**

Dear Sir,

This is to inform you that, PHE Dte. has undertaken a water supply project in the month of October 2018 in Bhargar-II block under the financial assistance of ADB and laying of foundation stone of the same was done by Hon'ble Chief Minister of West Bengal on 26th October 2018. Now the entrusted agency will start laying distribution network from 16.12.2019 in **Bhagabampur & Chaltaberia Gram Panchayet** along the road within ROW and a copy of drawing is herewith enclosed for your ready reference. In this matter you are requested to provide correct details of authorized person under your control regarding utilities & others if any during execution for smooth work progress without hampering existing services under your jurisdiction.

Your kind co-operation in this regard is requested.

Encls. : As stated.

Yours faithfully,

Memo No. _____/EE(C)PIUN24P,

Executive Engineer,
PIU, N-24 Pgs., WBDWSIP, PHE Dte.

Dated, New Town, the, _____

Copy forwarded for information to :-

- 1) The Sabhadhipati, South 24 Parganas Zilla Parishad.
- 2) The District Magistrate, South 24 Parganas.

Memo No. **1111 (23)**/EE(C)PIUN24P.

Executive Engineer,
PIU, N-24 Pgs., WBDWSIP, PHE Dte.

Dated, New Town, the, **13/12/2019**

Copy forwarded for information to :-

- 1) The Superintending Engineer, PIU, North 24 Parganas, WBDWSIP, PHE Dte.
- 2) The Assistant Engineer-II, PIU, N-24 Pgs., WBDWSIP, PHE Dte.
- 3) The Team Leader, DSISC-North 24 Parganas, WBDWSIP.
- 4) The Project Manager, NCC Ltd., Bhargar-II Project.

Executive Engineer,
PIU, N-24 Pgs., WBDWSIP, PHE Dte.

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhargar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 32 of 42 Original Issue Date :



Government of West Bengal
Office of the Executive Engineer
PIU, North 24 Parganas, WBDWSIP, PHE Dte.
Utility Building, Tank No.3, 2nd Floor, Block-AI,
Action Area-IA, New Town, Kolkata-700156
Phone No. : (033) 2324-2051, E-mail : ee.pnu24p.adb@wbphed.gov.in

Memo No. _____/EE(C)PIUN24P,

Dated, New Town, the, _____

To
The B.D.O. & Executive Officer,
Bhargar-II Development Block & Bhargar-II Panchayet Samiti,
South 24 Parganas.

Sub. : Design and construction of overhead reservoir including water supply distribution
network & metering works in Bhargar-II Block (Zone-15) Kachua.

Dear Sir,

You are well aware that the water supply project under reference is being going on within Bhargar-II block with financial assistance of ADB. Now the entrusted agency will start laying distribution pipe network from 16.12.2019 in Bhagabanpur & Chakuberia Gram Panchayet along the road within ROW and a copy of drawing is herewith enclosed for your ready reference.

Your kind co-operation in this regard is requested.

Encls. : As stated.

Yours faithfully,

Memo No. _____/EE(C)PIUN24P,

Dated, New Town, the, _____

Copy forwarded for information to :-

- 1) The Savapati, Bhargar-II Panchayet Samiti.
- 2) The Pradhan, Bhagabanpur / Chakuberia Gram Panchayet.
- 3) The Officer in Charge, Kashipur Police Station.

Memo No. 1112 (3-A) /EE(C)PIUN24P,

Assistant Engineer-II
PIU, N-24 Pgs., WBDWSIP, PHE Dte.

Dated, New Town, the, 13/12/2019

Copy forwarded for information to :-

- 1) The Superintending Engineer, P.I.U., North 24 Parganas, WBDWSIP, P.H.E. Dte.
- 2) The Executive Engineer, PIU, N-24 Pgs., WBDWSIP, PHE Dte.
- 3) Sri Samrat Banerjee, Junior Engineer, PIU, N-24 Pgs., WBDWSIP, PHE Dte.
- 4) The Team Leader, DSISC-North 24 Parganas, WBDWSIP.
- 5) The Project Manager, NCC Ltd., Bhargar-II Project.

Assistant Engineer-II
PIU, N-24 Pgs., WBDWSIP, PHE Dte.

Encls. : As stated

16/12/19
16/12/19

2470

Signature

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhargar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 33 of 42 Original Issue Date :



Government of West Bengal
Office of the Executive Engineer
PIU, North 24 Parganas, WBDWSIP, PHE Dte.
Utility Building, Tank No.3, 2nd Floor, Block-A1,
Action Area-IA, New Town, Kolkata-700156

Phone No. : (033) 2324-2051, E-mail : ee.pium24p.adb@wbphed.gov.in

Memo No. _____/EE(C)PIUN24P.

Dated, New Town, the, _____

To

- 1) The Station Manager,
WBSEDCL, Bhargar, South 24 Parganas.
- 2) The Sub Divisional Engineer,
HSNL, Canning Sub Division, Canning Telephone Exchange,
South 24 Parganas.

**Sub. : Design and construction of overhead reservoir including water supply distribution
network & metering works in Bhargar-II Block (Zone-15) Kachua.**

Dear Sir,

This is to inform you that, PHE Dte. has undertaken a water supply project in the month of October'2018 in Bhargar-II Block with financial assistance of ADB. Now the entrusted agency will start laying distribution network from 16.12.2019 in **Bhagabampur & Chaltaberia Gram Panchayet** along the road within ROW and a copy of drawing is herewith enclosed for your ready reference. In this matter you are requested to provide contract details of authorized person under your control regarding utilities & others if any during execution for smooth work progress without hampering existing services under your jurisdiction.

Your kind co-operation in this regard is requested.

Encls. : As stated.

Yours faithfully,

Sd/-
Assistant Engineer-II
PIU, N-24 Pgs., WBDWSIP, PHE Dte.
Dated, New Town, the, _____

Memo No. _____/EE(C)PIUN24P.

Copy forwarded for information to :-

- 1) The Savapadi, Bhargar-II Panchayet Samity.
- 2) The Executive Officer, Bhargar-II Panchayet Samity.

Sd/-
Assistant Engineer-I
PIU, N-24 Pgs., WBDWSIP, PHE Dte.
Dated, New Town, the, 13/12/2019

Memo No. 1143-1144 (2-4)/EE(C)PIUN24P.

Copy forwarded for information to :-

- 1) The Superintending Engineer, P.I.U., North 24 Parganas, WBDWSIP, PHE Dte.
- 2) The Executive Engineer, PIU, N-24 Pgs., WBDWSIP, PHE Dte.
- 3) Sri Samrat Banerjee, Junior Engineer, PIU, N-24 Pgs., WBDWSIP, PHE Dte.
- 4) The Team Leader, DSISC-North 24 Parganas, WBDWSIP.
- 5) The Project Manager, NCC Ltd., Bhargar-II Project.


Sd/-
Assistant Engineer-II
PIU, N-24 Pgs., WBDWSIP, PHE Dte.

2 - Connected Project Bhargar-II Zone-15-3-Arc

Time-10:45 AM
Date 16/12/19
Signature

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 34 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	

Appendix P.B: Labour License

GOVERNMENT OF WEST BENGAL
OFFICE OF THE DEPUTY LABOUR COMMISSIONER , BARUIPUR
*South 24 Parganas, Nandarani Complex (1st & 2 nd Floor) (Opp. 218 Bus Stand) Holding No - 474, Kulpi Road,
Ward No - 5, Shibaniipith, Baruipur, Kolkata-700144*

FORM VI
[See Rule 25(1)]

License No. : BRP04/CLL/000191 **Date : 27th Dec, 2018**

Lic Fees	1000
S.Deposit	30000

LICENSE

License is hereby granted to **NCC LIMITED** at **Patharghata, Block- Rajarhat , Barasat, PS - New Town, District - North 24 Parganas, Pin Code - 700156** under Section 12(1) of the Contract Labour(Regulation and Abolition)Act,1970 subject to the condition specified in Annexure.

The License shall remain till:-26th Dec, 2019

sd/-
Signature & Seal
Licensing Officer

RENEWAL

[Rule 29]

Renewal vide AIN No.	RENEWAL-LIC-009474-008133-26939-2019
1.Date of Renewal	21st Nov, 2019
2.Fees paid for Renewal	₹ 1250 (One Thousand Two Hundred Fifty rupees only)
3.Date of Expiry	26th Dec, 2020

SHREEJITA SAHA
Digitally signed by SHREEJITA SAHA
Date: 2019.11.21 00:57:48 +05'30'
Signature & Seal
Licensing Officer

1 of 3

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 35 of 42 Original Issue Date :

Appendix P.C: Workman Compensation

FUTURE GENERALI
TOTAL INSURANCE SOLUTIONS

Workmen's Compensation Policy- Policy Schedule

Policy Servicing Office :	Off Code-15, Future Generali India Insurance Co Ltd, 1st Floor D.No.7-1-21A, APDL Estate Opp. Country Club, Begumpet, Hyderabad, Telangana, Pincode-500016., Tel. No : 040-66038600		
Policy No :	2019-16129169-FWC	Period of Insurance :	From 00:00 04/02/2019 To Midnight of 03/02/2020
Insured :	NCC Limited	Intermediary Name/Code :	INDIA INSURE RISK MANAGEMENT AND INSURANCE BROKING SERVICES/0001521
Address :	BHANGAR II BLOCK, South Twenty Four Parganas, West Bengal, 743302	Telephone (Ablet, Off, Home) :	4027822990/00892590738/4027822990
		Fax No & Email Id :	02256791416 / PADMAJA.SURYARAJAN@INDIAINSURE.COM
GSTIN Number :	19AAACH7235C1Z66	PGI GSTIN Number :	36AABCP0919K1ZA

In consideration of the Policy holder covered herein paying to the Future Generali India Insurance Company Limited (herein after called the Insurer) the premium as stated in the Schedule and in reliance upon the statements made by the Policy holder in the proposal including its attachment or otherwise, and the material misrepresentation therein, the Insurer agrees to provide insurance against loss/damage liability or expense to the extent and in the manner herein provided subject to all terms, conditions, exceptions and warranties hereinafter set forth.

Co-insurance Details		Schedule Of Premium (₹)	
Insurer	Share (in %)	Gross Premium	134,304.36
FUTURE GENERALI INDIA INSURANCE COMPANY LIMITED	100%	Goods and Service Tax	24,174.18
		Total Premium	158,478.50

Block Details

Nature of Business : Design and Construction of overhead reservoir included in water supply distribution and metering works in Bhangar II Block

Location : Design and Construction of overhead reservoir included in water supply distribution and metering works in Bhangar II Block

Contractor/Sub-Contractor Name : NCC LTD

No of Employees	Description of work done by Employees	Declared Wage during the Period of Insurance (₹)
30	Highly Skilled workers	6,642,000.00
30	Skilled workers	6,048,000.00
30	Semi Skilled Workers	3,490,000.00
30	Unskilled Workers	4,388,000.00
Total		21,168,000.00

Coverage Details

The Policy covers Liability of the Insured under the following Law(s) shown as covered, subject to claim being otherwise admissible as per terms, conditions and exclusions of the Policy and subject to Limit of Indemnity as stipulated against each Law:

Law	Limit of Indemnity	Coverage
Employee's Compensation Act, 1923 and subsequent amendments thereon as in the date of issue of this Policy	Subject otherwise, to the terms, conditions & except Exclusions of the Policy, the amount of liability incurred by the Insured	Yes
Common Law Fatal Accident		Yes

Law(s)

WC Act 1923 and subsequent amendment of the said Act prior to the date of issue of the policy provided that the insurance granted hereunder is not extended to include:

1. Any interest and/or penalty imposed on the insured on account of his/her failure to comply with the requirements laid down under WC Act 1923

2. Occupational disease of any kind

Additional Clauses, Conditions, Warranties & except Exclusions

Termination is excluded from coverage.

No cover for Medical Expenses, unless specifically allowed in the policy.

No Cover for Medical Expenses.

No Cover for occupational Diseases

Insulation/Territory: India

Excluding War Risk, Blasting, Trenching and Handling of Explosives

Excluding loss arising out of insurrection and actions of fire or rioting

Warranted that safety practices are followed by the workers in light

Contractors and sub-contractors/employees are covered.

Important:- 1. All other Terms, Conditions and Exclusions as per attached Policy Wording. 2. In case of payment by cheque, in the event of dishonor of cheque for any reason whatsoever, insurance provided under this document automatically stands cancelled from the inception irrespective of whether a separate communication is sent or not.

For Future Generali India Insurance Co. Ltd.

Sharda
(Authorized Signatory)

Receipt No : Z8665378
Date of Issue : 07/02/2019
Place of Issuance : Mumbai*

*Address mentioned below.

Note: This document is digitally signed by Sharda Ramakrishnan, Authorized Signatory of Future Generali India Insurance Company Limited on 07/02/2019

The stamp duty of Rs 67.35 paid by Letter Of Authorization No. CSD/18/2018/3179/18, dated 16/08/2018, Mumbai - 5017/C.R.9594-1, dated 09/01/2018.

Product UIN : IB-DAN132P0012V01200708

Future Generali India Insurance Company Limited, Corporate & Registered Office: 6th Floor, Tower - A, IndiaBulls Finance Centre, Banganga Depot, Mang. Bhikshane Road, Mumbai - 400013, Maharashtra (CIN No: 1808-216-213, 1809-500-3333, 822-47837800, Email: fgi@futuregenerali.in, Website: www.futuregenerali.in RDA Regn No. 132, CIN - U66010MH2006PL1C161387.

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 36 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	

Appendix P.D: PUC Certificates

POLLUTION BRUSH CONTROL CERTIFICATE
(Under the West Bengal Motor Vehicles Rules, 1988)

Vehicle Registr. No. **JH 01N 7488** WB-01-D 5972591

Date of Issue: **06/11/2019** Valid upto: **05/05/2020**

Pollution Level

CO (%)	0.000
HC (ppm)	
SO (HSU)	

PUC Certificate issued by: **[Signature]** License No. and Seal: **32/P**

COMPUTERISED EMISSION TEST CERTIFICATE
Authorised by Transport Dept. of West Bengal

AKBAR AUTO EMISSION TESTING CENTRE WB-01-D 5972591
ASANTI HIGHWAY, GHATAKPUKUR, PO:PS-BHANGAR, 24PGS(S), PIN-743502

UC No:- 009480 Licence No :- 32/P

Vehicle No :- JH 01N 7488 Test Date :- 06/11/2019

Year Of Reg :- 2000 Test Time :- 3:59:10 AM

Speedo Meter :- 2221 Fuel :- Petrol

Vehicle Make :- HERO_HONDA Test Fee :- 80

Vehicle Model :- CD-DELUX Vehicle Type :- 2W

Engine Number :- 09368 Engine Type :- 4S

Chassis Number :- 03818 Result :- Pass

Vehicle Color :- BLACK Valid Upto :- 05/05/2020

Compliant :- Non BS

Contact :- 7995958341

Owner :- N. C. C. LTD

IDLE EMISSION

	Regulation	Actual	
Ideal CO :-	3.5	0.000	%VOL
CO corrected :-	3.5	0.000	%VOL
Idle HC :-	4500	0	PPM
CO2 :-		0.00	%VOL
O2 :-		27.58	%VOL
NOx :-		0	%VOL
Lambda :-		0.000	
PEF :-		0.544	
RPM :-		00000	
AFR :-		00000	
Oil Temp :-		00000	°C

HIGH IDLE EMISSION

CO :-	0.2		%VOL
CO2 :-			%VOL
O2 :-			%VOL
Lambda :-			
RPM :-			

Name of Authorise Signatory
with Seal of Testing Center

AKBAR AUTO EMISSION TESTING CENTRE

POLLUTION UNDER CONTROL CERTIFICATE
(Under the West Bengal Motor Vehicles Rules, 1988)

Vehicle Registr. No. **PB02BL7373** WB-01-**D 5679142**

Date of issue: **16-08-2019** Valid upto **15-02-2020**

Pollution Level

CO (%)	
HC (ppm)	
Nox (ppm)	5.83

PUC Certificate No. **32/D**

Signature **32/D**

WB-01- D 5679142

COMPUTERISED EMISSION TEST CERTIFICATE
CMVR AUTHORISED BY : Govt. of we
AKBAR AUTO EMISSION TESTING CENTRE
BASANTI HIGHWAY, GHATAKPUKUR, PO/PS-BHAGAR, 24 PGS (S), W.B-743502

I.D Number **WB32D3647572** Licence No: **32/D**
Year Of Registration= **2011** Date : **16-08-2019**
vehicle registration no = **PB02BL7373** TIME= **02:47:14**
Speedometer Reading[kms] = **21522** Owner= **N C C CO**
Engine Number=**9218** Driver:- **SELF**
chasis Number=**G2011** Test Fee : **Rs.100/-**
Vehicle Colour = **YELLOW** Fuel : **Diesel**
Vehicle Make : **JCB** Smk cell Temp : **00**
Vehicle Model : **3DX** Oil Temp : **93.0**
Type Of Engine : **OTHERS** Valid Up To : **15-02-2020**
Type OF Vehicle: **OTHERS** Grade **32/D**

Test Result : Free Acceleration Validity **6 Months**

	ideal Rpm	max Rpm	K Value	Hsu_val	Oil Temp
1	860	2900	5.37	90.06	81
2	860	2900	0.17	6.9	68
3	852	2700	0.12	6.9	66
Avg	860	2930	1.9	55.83	

Seal Of Testing Center

Certified that this Vehicle's K-Mean and Hsu% value conforms to the standards prescribed under rule 115(2) of CMB rules 1989, Operator:- **MD RAMIZ RANA**

POLLUTION UNDER CONTROL CERTIFICATE
(Under the West Bengal Motor Vehicles Rules, 1989)

Vehicle Registrn. No. **WB15B2529** WB-01-**D 5678745**

Date of issue: **23-07-2019** Valid upto **22-01-2020**

Pollution Level
CO (%) **66.83**
HC (ppm) **66.83**
SD (HSU) **66.83**

PUC Certificate issued by: **AKBAR AUTO EMISSION TESTING CENTRE**

Signature: **[Signature]**

WB-01-D 5678745

COMPUTERISED EMISSION TEST CERTIFICATE
CMVR AUTHORISED BY : Govt. of WB
AKBAR AUTO EMISSION TESTING CENTRE
BASANTI HIGHWAY, GHATAKPUKUR, PO/PS-BHAGAR, 24 PGS (S), W.B-743502

I.D Number **WB32D3647596** Licence No: **32/D**
Year Of Registration= **2011** Date : **23-07-2019**
vehicle registration no = **WB15B2529** TIME: **05:46:14**
Speedometer Reading[kms] = **2541** Owner: **NABA KUMAR GHOSH /851304**
Engine Number= **28746** Driver: **SELF**
chasis Number= **B5954** Test Fee : **Rs.100/-**
Vehicle Colour = **OTHERS** Fuel : **Diesel**
Vehicle Make : **HMT** Smk cell Temp : **00**
Vehicle Model : **4022** Oil Temp : **93.0**
Type Of Engine : **OTHERS** Valid Up To : **22-01-2020**
Type OF Vehicle: **OTHERS** Grade : **[Redacted]**

Test Result : Free Acceleration Validity **6 Months**

	ideal Rpm	max Rpm	K Value	Hsu val	Oil Temp
1	860	2900	5.37	90.06	61
2	860	2900	0.17	6.9	68
3	852	2700	0.12	6.9	66
Avg	860	2930	1.9	55.83	

AKBAR AUTO EMISSION TESTING CENTRE

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhangar-II Block	Doc. No. NCC/ SEMP /01
	Site Specific Environmental Management Plan	Last Revision No. 00 Last Revision Date : 00 Page 39 of 42 Original Issue Date :

POLLUTION UNDER CONTROL CERTIFICATE
(Under the West Bengal Motor Vehicles Rules, 1989)

Vehicle Register No: **WB08G1752** WB-01: **D 4231066**

Date of Issue: **07-May-2019** Valid upto: **06-May-20**

Pollution Level:

CO (%)	
HC (ppm)	
SD (BSU)	44.1%

PUC Certificate issued by: **MIL ENTERPRISE** License No. and Seal: **151/AETC/2018**

Signature: *[Signature]* Vehicle Pass: **WB-01: D 4231066**

POLLUTION UNDER CONTROL CERTIFICATE
(Under the West Bengal Motor Vehicles Rules, 1989)

MIL ENTERPRISE
BP RAJARHAT NEW TOWN, KOLKATA - 700156, WEST
PH: 9432010995

Transport Department

Label Code: **WB** Licence No: **151/AETC/2018** Test Station Code: **0001**

PUC No.: **FWB0001000006** Vehicle Reg No: **WB08G1752**

Name: **NCC LIMITED** Category: **car**

Address: **NEW TOWN** Make: **MAHINDRA**

KOL-156 Model: **BOLERO**

Mobile: **9630728872** Date of Reg.: **2019**

Date: **07-May-2019** Speedo mtr Rdg: **252**

Time: **11:17 AM** Engine No.: **16260**

Fuel: **Diesel** Chassis No.: **32097**

Flushing Cycle Mean: **RPM Min: 0820 RPM Max: 1923** Emission Norms.: **BS IV or Onwards**

Vehicle Type: **BS4 - 4 Wheeler**

SNo.	RPM min	RPM max	K m-l	BSU %	OTP C
1	0710	2050	01.23	41.2	042.00
2	0720	2110	01.47	46.9	041.00
3	0725	2080	01.36	44.2	041.00

Standard	Measured
K m-l	1.62 01.35
BSU %	60 44.1

Valid upto: **06-May-20**

Grade: **B**

Test Fee: **100**

Mean **0716 2080 01.35 44.1% 041.33**

This vehicle meets Emission Standards Prescribed under Rule 115(2) of Central Motor Vehicle Rule's 1989.

Seal of Testing Centre

Authorized Signatory

JNDUS DiesX 2.8.6/0000-0000/4660

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhargar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 40 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	

Appendix P.2: Contractor's OHS Policy Statement

NCC LIMITED

Health, Safety & Environment Policy

For Construction/Erection and Commissioning, the General Strategic Objectives Listed Below are Followed:

- A proactive, role model HSE at Site.
- All Sites related activities and Office Work will result in no one getting injured or made unwell.
- Early identification of hazards and risk and the decision or adequate measures.
- Reduction of negative impact on the neighborhood are the the environment in particular on fauna and flora to a minimum.
- Provide training in HSE knowledge and encourage continuous improvement and development of this.
- Continuous monitoring of the HSE performance.
- Promote the benefits of a healthy life-style amongst our employees.
- Report and investigate accidents and incidents to take lessons and prevents similar events occurring again.
- Preserve ecological balance and heritage.

Prepared by:	Copy No.	Date of Issue:	Approved by:	Issued by:

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhargar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 41 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	

Appendix P.3: Sample Grievance Registration Form

(Available in Bengali and English)

The _____ Project welcomes complaints, suggestions, queries, and comments regarding project implementation. We encourage persons with grievance to provide their name and contact information to enable us to get in touch with you for clarification and feedback.

Should you choose to include your personal details but want that information to remain confidential, please inform us by writing/typing *(CONFIDENTIAL)* above your name. Thank you.

Date	Place of registration	Project Town			
		Project:			
Contact information/personal details					
Name		Gender	* Male * Female	Age	
Home address					
Place					
Phone no.					
E-mail					
Complaint/suggestion/comment/question Please provide the details (who, what, where, and how) of your grievance below:					
If included as attachment/note/letter, please tick here:					
How do you want us to reach you for feedback or update on your comment/grievance?					

1. FOR OFFICIAL USE ONLY

Registered by: (Name of official registering grievance)	
Mode of communication: Note/letter E-mail Verbal/telephonic	
Reviewed by: (Names/positions of officials reviewing grievance)	
Action taken:	
Whether action taken disclosed:	Yes No
Means of disclosure:	

NCC LIMITED	Design and Construction of Overhead Reservoir Including Water Supply Distribution Network and Metering Work in Bhargar-II Block	Doc. No. NCC/ SEMP /01 Last Revision No. 00 Last Revision Date : 00 Page 42 of 42 Original Issue Date :
	Site Specific Environmental Management Plan	

অভিযোগ/ পরামর্শ/ মন্তব্য/ প্রমাদি লিপিবদ্ধ করার নমুনা পত্র

এই প্রকল্পটি সৃষ্ট ও সুন্দরভাবে রূপায়নের উদ্দেশ্যে সকলের অভিযোগ, পরামর্শ, প্রশ্ন এবং মন্তব্য প্রত্যাশা করে। আপনার কোনও অভিযোগ থাকলে আপনার নাম ও যোগাযোগের ঠিকানা দিয়ে আমাদের সহযোগিতা করবেন, আপনার অভিযোগ / প্রশ্নের যথার্থ সদুত্তর ও আপনাকে পরিস্থিতি সম্পর্কে আমরা অবগত করবো।

যদি আপনি আপনার ব্যক্তি পরিচয় গোপন রাখতে চান তাহলে আপনার নামের উপরে " গোপনীয় " কথাটি লিখবেন।

ধন্যবাদান্তে

তারিখ	পঞ্জীকরণের বা Registration এর স্থানঃ ব্লক- গ্রাম পঞ্চায়েত- গ্রাম সংসদ-		
যোগাযোগের ঠিকানা / ব্যক্তিগত তথ্য			
নাম		লিঙ্গ	বয়স
বাড়ির ঠিকানাঃ গ্রাম- ফোন নং-	পাড়া- ই-মেইল-	পুরুষ - মহিলা-	
অভিযোগ/ পরামর্শ/ মন্তব্য/ প্রমাদি- দয়া করে কে, কি, কোথায় এবং কিভাবে - অভিযোগের এই বিশদ বিবরণ নিচে লিখুন-			
যদি কোন অতিরিক্ত কাগজ জুড়তে হয় / বা নোট থাকে বা চিঠি থাকে তাহলে এই ঘরে (✓) টীক দিন।			
আপনি কিভাবে আপনার অভিযোগ / মন্তব্য বিষয়ে অবগত হতে চান ?			

সুধুমাত্র অফিসের ব্যবহারের জন্যঃ

যে আধিকারিক অভিযোগ জমা নিলেন তার নাম :
কিভাবে জানানো হল (✓) টীক দিনঃ নোট বা চিঠির মাধ্যমে – ই-মেইল- মুখে মুখে বা টেলিফোনে-
যিনি অভিযোগ প্যারার পর খতিয়ে দেখেছেনঃ
(নাম / পদ)
কি ব্যবস্থা গ্রহণ করা হয়েছেঃ
ব্যবস্থা যা গৃহীত হয়েছে তা জানানো হয়েছে কি না - হ্যা / না
কিভাবে জানানো হলঃ

মন্তব্য-

প্রস্তুতকারক -

আনুমদনকারী -

তারিখ-
